

2016 Transportation Sales Tax – Featured Projects Update (9-26-2024)

- Airport Area Roads Improvements
 - Palmetto Commerce Interchange (<https://www.palmettocommerceinterchange.com/>) – Project is currently under construction with construction completion anticipated in early 2026.
 - Airport Connector Road (<https://www.airportconnectorroad.com/>) – Project’s Environmental Assessment (EA) was approved by FHWA in May 2024. Currently awaiting Record of Decision from FHWA before proceeding with right-of-way acquisition. Anticipate starting construction of project in 2026.
 - Palmetto Commerce Parkway Phase 3 (<https://www.palmettocommerceparkway3.com/>) – Currently engaged with Joint Base Charleston on partnering agreement regarding acquisition of easements from Joint Base Charleston and working through environmental permitting process. Anticipate starting construction in 2028.

- Dorchester Road Widening (Michaux Parkway to County line) (<https://www.dorchesterroadimprovements.com/>) – Initial design concepts have been developed and will be presented to the public at a later date, to be determined, after cancelling the Public Information Meeting scheduled for September 26th due to inclement weather. Currently anticipate starting construction in 2028

- US-17 at Main Road flyover and widening Main Road from Bees Ferry to Betsy Kerrison (<https://www.mainroadcorridor.com/>)
 - Main Road Segment A (Bees Ferry to River Road) – Design-Build contract was recently awarded with groundbreaking ceremony on September 26th. Anticipate construction completion by end of 2028.
 - Main Road Segment B (River Road to Maybank Hwy) – On Hold – Traffic analysis shows improvements not needed with Mark Clark Extension
 - Main Road Segment C (Maybank Hwy to River Road) – Currently developing preliminary plans and making scope reductions at request of Council to limit impacts to businesses, residences, and the natural environment.

- Glenn McConnell Parkway (<https://roads.charlestoncounty.org/projects/glenn-mcconnell/>) – Project has been completed.

- James Island Intersection and Pedestrian Improvements (<https://roads.charlestoncounty.org/projects/james-island/>)
 - Fort Johnson Road & Secessionville Road Intersection Improvements – Project has been re-advertised for construction bids.

- Fort Johnson Road & Camp Road Intersection Improvements – *Project is currently in the right-of-way acquisition phase. Anticipate starting construction in spring of 2025.*
 - Central Park Road & Riverland Drive Intersection Improvements – *Project is currently in the design phase with right-of-way acquisitions scheduled to begin in 4th Quarter 2024. Anticipate starting construction in fall of 2025.*
 - Folly Road Bike & Ped Improvements – *Design work has been completed. Project was advertised for bids earlier this year, but none were submitted. Anticipate re-advertisement of project in 4th Quarter 2024.*
- Northside Drive Realignment at Ashley Phosphate Road – *ON HOLD, Not needed if Palmetto Commerce Parkway Phase 3 is constructed.*
 - Savannah Highway/Ashley River Bridges/Crosstown Congestion Infrastructure Improvements – *Study recommending improvements has been completed. Pedestrian bridge over Ashley River is currently under design through City of Charleston.*
 - Savannah Highway Capacity and Intersection Improvements (<https://www.savannahhighway.com/>) – *Project is currently in the right-of-way acquisition phase. Anticipate starting construction in mid-2025.*
 - US-78 Improvements (US-52 to County line) (<https://hwy78corridor.com/>) – *Public Information Meeting on conceptual designs was held earlier this year with public comments. Design work is progressing with work towards environmental permitting. Currently anticipate starting construction in early 2027.*
 - SC-41 Improvements (US-17 to Wando Bridge) (<https://www.hwy41sc.com/index.html>) – *Construction on interim improvements at the intersections of SC 41/US 17/Dingle Road and SC 41/Joe Rouse Road are underway with anticipated completion in November 2024. Overall project is working through environmental permitting process with construction anticipated to start in 2027.*

TODAY

2009

2013

2017

2021

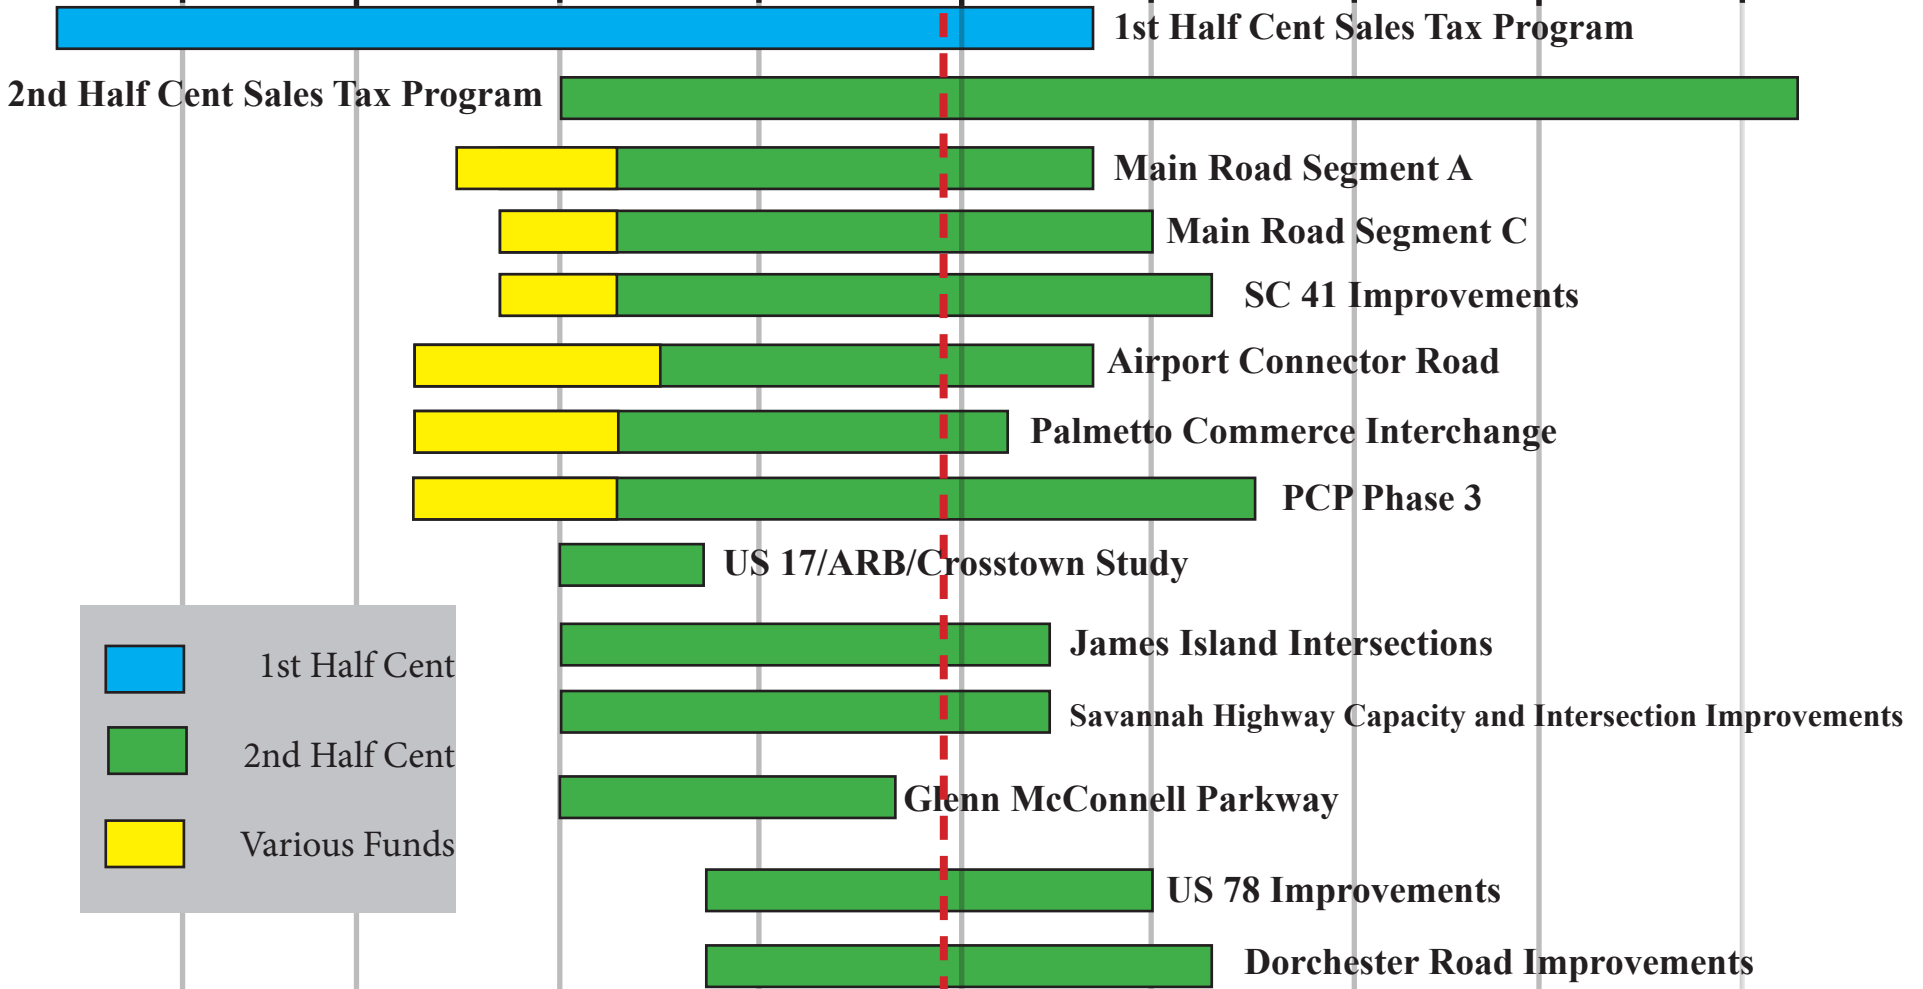
2025




2029

2033

2037

2041



	1st Half Cent
	2nd Half Cent
	Various Funds
